

# SOUTHERN REGION GRMP SITE INSPECTION FORM



| SITE NUMBER AND NAME:<br>S004 Willow Creek (North of Fort |                     | HIGHWAY & KM: 2:08, 6.284             |         | PREVIOUS         | INSPECTION DATE:  May 29, 2024 |  |
|---|---------------------|---------------------------------------|---------|------------------|--------------------------------|--|
|   |                     |                                       |         | INSPECTION DATE: |                                |  |
| Macleod)  |                     |                                       |         | May 10, 2023     | ay _e, _e_ :                   |  |
| LEGAL DESCRIPTION:  | NAD 83 COORDINATES: |                                       |         | RISK ASSESMENT:  |                                |  |
| 13/14-20-09-26-W4M  | UTM N               | lorthing                              | Easting | PF: 9 CF: 4 TC   | OTAL: 36                       |  |
|   | 12 5                | 514351                                | 320169  |                  |                                |  |
| Average Annual Daily Traffic (A                           | AADT):              | CONTRACTOR MAINTENANCE AREA (CMA): 26 |         |                  |                                |  |
| 5000 (north) & 5720 (south) (R                            | eference No         |                                       |         |                  |                                |  |

| SUMMARY OF SITE INSTRUMENTATION:   | INSPECTED BY:           |
|--|-------------------------|
|  | Chris Grapel (KCB)      |
| Four slope inclinometers, six standpipes, and six vibrating wire piezometers are     | Peter Roy (KCB)         |
| located at the crest of the slide. Instruments located in the slide mass are assumed | Kristen Tappenden (TEC) |
| to be inoperable.  | Alex Frotten (TEC)      |
| to be ineperable.  | 7 liox 1 rollor (120)   |
|  |                         |

LAST READING DATE: May 15, 2024

PRIMARY SITE ISSUE: Landslide at outside bend of Willow Creek (slope crest retrogressing), possibly due to infiltration from irrigation activities on farmland on the opposite side of Hwy 2. Landsliding has retrogressed into eastbound lane ditch, causing ditch flows to discharge onto the slide surface.

APPROXIMATE DIMENSIONS: The site is approximately 400 m long and 20 m in height. The head scarp is located approximately 11 m to 12 m from the guardrail. The slope is approximately 4H:1V to 5H:1V.

DATE OF ANY REMEDIAL ACTION: 2008 – slope stabilization (soil nailing, grading, and bioengineering (live staking)) with longitudinal peaked stone creek bank (LPSTP) armouring to reduce erosion at the toe of the slide. 2014 – installation of a guardrail along the east (northbound) edge of the highway.

| ITEM              | CONDITION<br>EXISTS |    | DESCRIPTION AND LOCATION   | NOTICABLE<br>CHANGE<br>FROM LAST<br>INSPECTION |    |
|-------------------|---------------------|----|--|--|----|
|                   | YES                 | NO |  | YES  | NO |
| Pavement Distress |                     | Х  | Transverse pavement cracking but is not believed to be attributed to the slide.  |  | Х  |
| Slope Movement    | X                   |    | The head scarp of the slide has been retrogressing into the ditch since 2016. The head scarp has retrogressed over 10 m in the last 10 years. No significant changes noted compared to 2023. |  | X  |
| Erosion           | Х                   |    | Erosion observed on slopes from ditch discharge onto slide area, riprap armouring placed in 2008 is intact.  |  | Х  |
| Seepage           | X                   |    | N/A – none observed during the 2024 inspection.  |  | Х  |
| Culvert Distress  |                     | Х  | N/A – none observed  |  | Х  |

### **COMMENTS**

There has been minimal change in slope retrogression observed between 2023 and 2024. The head scarp is approximately 11 m to 12 m from the guardrail at the closest point. South of the main slide, the right flank has retrogressed to approximately 16 m from the guardrail. There are three wooden stakes present at the head scarp that are used to estimate slide retrogression. The south stake is 1.3 m to the scarp, north stake is 0.75 m to the scarp, and the middle stake, where the scarp furthest into the ditch is 1.0 m to the scarp. There has been minimal changes measured since 2023. It is estimated that there has been 2.5 m to 3.5 m of retrogression into the ditch since 2016.



# SOUTHERN REGION GRMP SITE INSPECTION FORM



The head scarp has retrogressed 3 m to 5 m past the fence line. The slide zone is actively being undermined and material from the topsoil mat is sloughing into the slide zone over time. No significant changes were noted in the slide mass during the 2024 inspection.

The site was well vegetated during the 2024 inspection. However, bare patches of soil were observed near the top of the slide zone.

A buried black utility cable is exposed in the slide area.

The nature of the slide (i.e., back tilting blocks) suggests a combination of rotational and translational failure along a deep weak layer. The right flank of the slide (southeast) appears to be retrogressing faster than the left flank (northwest).

The creek armouring completed in 2008 is in good condition. However, continued slope movement is displacing the armouring eastward across creek, straightening a former curved zone of creek bank. The riprap is exposed due to low water levels and needs maintenance to the vanes.

#### Discussed Remedial Actions:

### Short-Term

- The operable instruments should continue to be read twice per year (spring and fall) as part of the Southern Region GRMP.
- Data loggers were installed in spring 2023 at all three VWP locations (6 VWPs in total) to gather data on seasonal groundwater fluctuations, irrigation impacts and precipitation events.
- A desktop study should be completed for the site including review of existing borehole logs, geological maps, reviewing historic air photos, and assessing available LiDAR data for use in change detection.

### Long-Term

- A geotechnical site investigation should be completed to assess the subsurface conditions (i.e., stratigraphy and groundwater conditions).
- Preliminary engineering should be completed to assess repair options for the site. Potential repair options for this site include: diverting surface water away from the slide zone; or installing horizontal drains connected to a seepage collection curtain. The seepage collection curtain would need to be assessed for potential impact to the farmland and reservoir on the west side of the highway. A proposal for this work was issued in March 2023.



# SOUTHERN REGION GRMP SITE INSPECTION FORM




This report is an instrument of service of Klohn Crippen Berger (KCB). The report has been prepared for the exclusive use of Alberta Transportation and Economic Corridors (Client) for the specific application to the Southern Region Geohazard Risk Management Program (Contract No. CON0022161) and it may not be relied upon by any other party without KCB's written consent.

KCB has prepared this report in a manner consistent with the level of care, skill and diligence ordinarily provided by members of the same profession for projects of a similar nature at the time and place the services were rendered. KCB makes no warranty, express or implied.

Use of or reliance upon this instrument of service by the Client is subject to the following conditions:

- (i) The report is to be read in full, with sections or parts of the report relied upon in the context of the whole report.
- (ii) The observations, findings and conclusions in this report are based on observed factual data and conditions that existed at the time of the work and should not be relied upon to precisely represent conditions at any other time.
- (iii) The report is based on information provided to KCB by the Client or by other parties on behalf of the client (Client-supplied information). KCB has not verified the correctness or accuracy of such information and makes no representations regarding its correctness or accuracy. KCB shall not be responsible to the Client for the consequences of any error or omission contained in Client-supplied information.
- (iv) KCB should be consulted regarding the interpretation or application of the findings and recommendations in the report.
- (v) This report is electronically signed and sealed and its electronic form is considered the original. A printed version of the original can be relied upon as a true copy when supplied by the author or when printed from its original electronic file.

Peter Roy, P.Eng. Civil Engineer

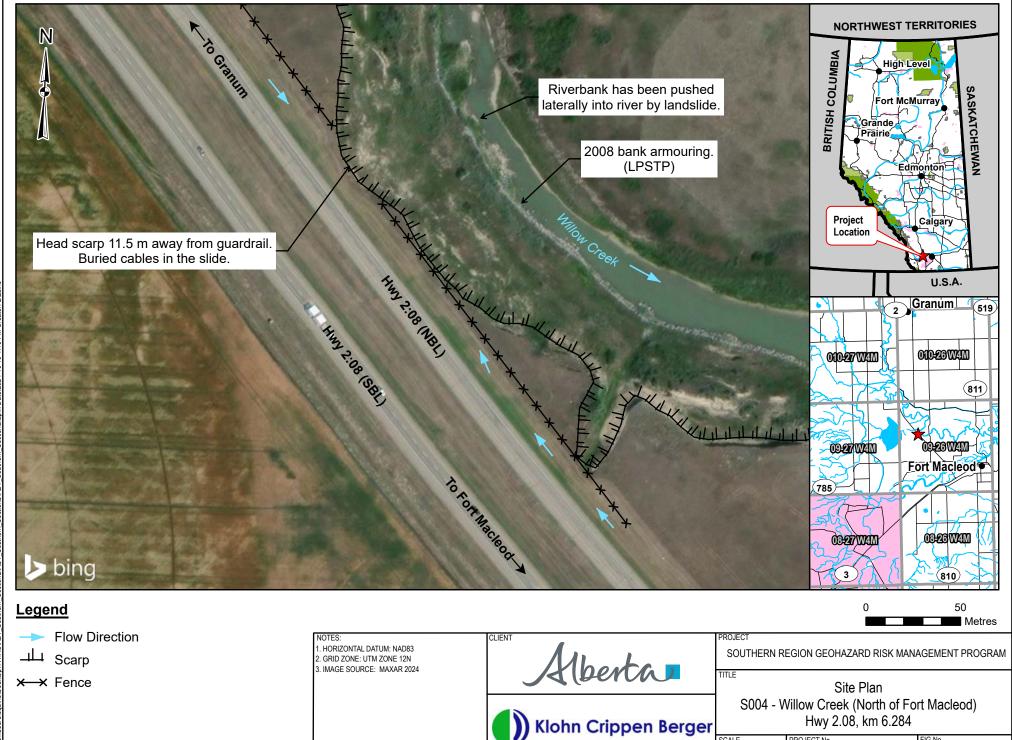

SCALE

A05116A03

Photo 1 Slide area. Photo taken facing west on May 10, 2023.



Photo 2 Head scarp located up to 5 m past the fence line. Photo taken facing north on May 29, 2024.



Photo 3 Head scarp located up to 5 m past the fence line. Photo taken facing south on May 29, 2024.

